

Kris Schwab

Core Facility Solutions

9/9/2021 | 3 Photos




**CORE FACILITY**  
— SOLUTIONS —


# Trinity Lutheran Church of Bismarck

Weekly Report For Week Ending 9/10/2021

# Section 1

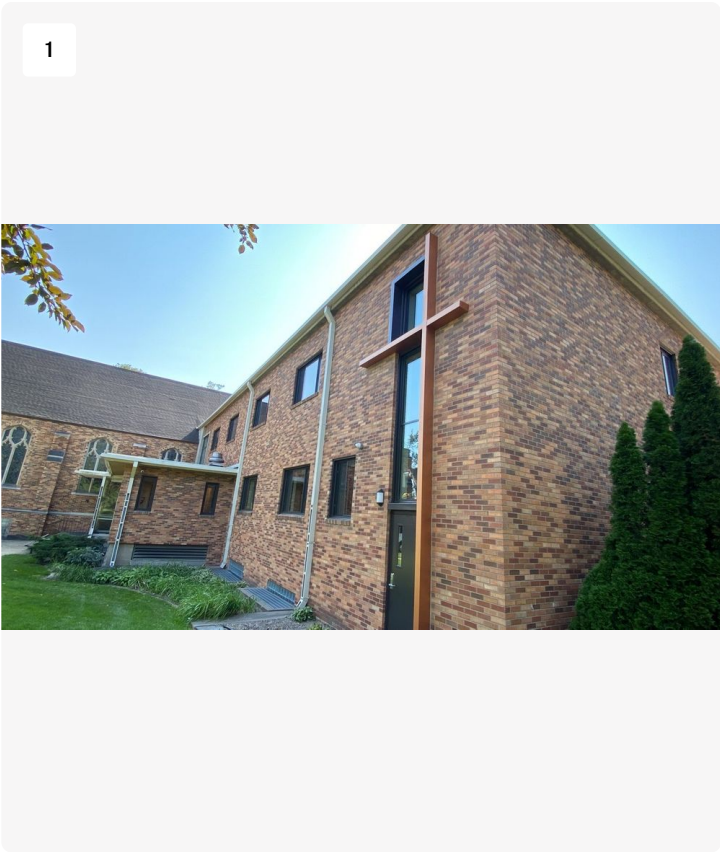

Cross at the northeast entrance finished.

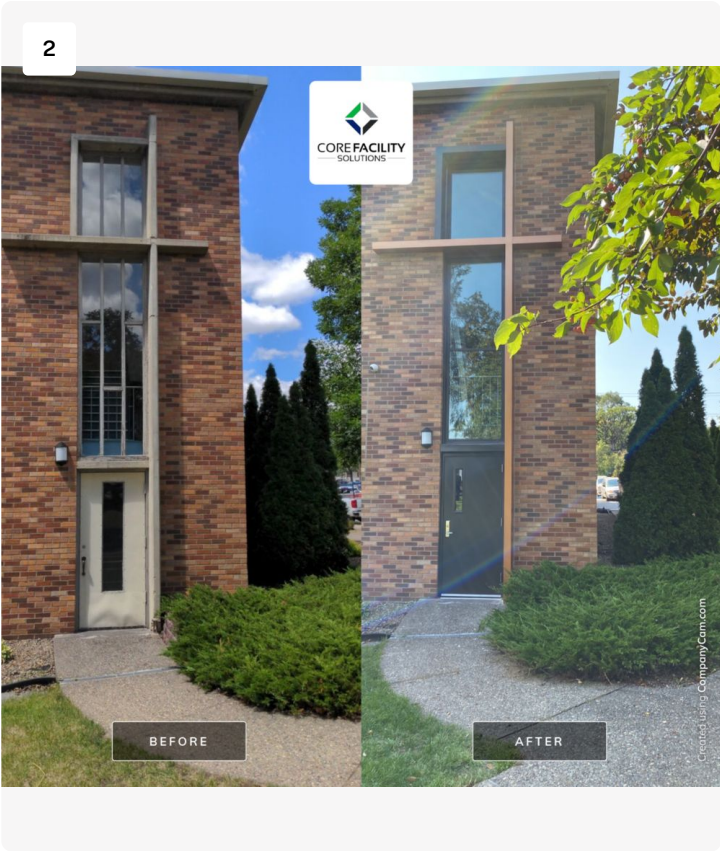

Before and after photos of the northeast entrance.



Before and after photos of work completed on the east side of the building.

Project: Trinity Lutheran  
Date: 9/9/2021, 3:48pm  
Creator: Kris Schwab  
Tags: Before and After

## Section 2

Progress as of this week:

Straightway has completed all work on site and is down to some minor punch list items. The wrap on the Cross look beautiful! Straightway has done an excellent job and has been great to work with.

City Air Mechanical has the blower coil in the nursery installed. Some minor work is needed to make sure there is access to the unit's air filters so maintenance is not difficult in the future. Core is working with City Air on a solution. The chiller piping has started, due to some unforeseen obstacles City Air and Core have had to come up with a new route for the chiller piping.

Johnson Controls is working on updates to the temperature control drawings.

Plan for next week:

Core will continue to work with all contractors to ensure project runs smoothly.

City Air Mechanical will be back to work on the chiller piping.

Items of note:

Air handling equipment should continue to arrive throughout the next couple weeks.

Core hopes to receive the fire alarm engineering from Johnson Controls/Simplex very soon, then we can start getting bids from electrical contractors and start gaining approval from the City of Bismarck. The rep for Simplex is making an initial call to the Fire Inspector to get the ball rolling. The Council has asked Core to look at structural issues occurring in the 1930 building. Core has visited with a Structural Engineer onsite to start investigating the issues.

Core has received pricing for fence around the chiller but waiting for the security gate for the Peace Chapel.
